



COMMERCIAL ASSESSMENT

nice 2 network

Project value, work completed, readiness, operating cost and 10% buyout

£140k	70%	£14k
current project value	overall readiness	recommended 10% buyout now

Prepared by IntAillium for the nice2 company

Assessment date: 19 August 2026

Commercial planning document - figures exclude VAT and tax

Executive summary

A decision-ready view of what exists, what it is worth, and what remains.

197 COMMITTS REVIEWED	114 API ROUTES	70 DATA TABLES	230 AUTOMATED TESTS
---------------------------------	--------------------------	--------------------------	-------------------------------

Bottom line

nice 2 network is a substantial, working social and project collaboration platform, not a prototype landing page. The production build compiles, the data model is extensive, and the product includes authentication, profiles, projects, matching, messaging, meetings, administration, safety controls and analytics.

It is best classified as controlled-beta ready. It is not yet a clean public-launch release because one automated test fails in the current working tree, lint has 35 errors, deployment configuration and operational controls require completion, and the current media and live-meeting architecture will become inefficient as membership grows.

Commercial measure	Recommended figure	Meaning
Equivalent work completed	£134,250	1,790 equivalent professional hours at a blended solo rate of £75/hour.
Current as-is project value	£140,000	Rounded replacement value including reusable IP, brand implementation and delivery acceleration.
10% handover buyout now	£14,000	Ten percent of current value for the coding handover and transfer of the agreed service projects to the nice2 founders.
Completion investment	£45,713	Estimated 530 hours plus 15% contingency, including technical SEO completion.
Completed project value	£186,000	Rounded replacement value after the priority completion plan is delivered and evidenced.
10% handover buyout at completion	£18,600	Ten percent of the estimated completed value.

Recommended commercial position

If the development work has not already been paid for, the present settlement is £148,250: £134,250 work-to-date fee plus £14,000 handover buyout.

If the work-to-date fee has already been paid, the current coding and service-project handover buyout is £14,000 only.

If IntAillium completes the release-hardening programme before transfer, reprice the handover buyout against the completed value: £18,600, with completion work billed separately.

These are commercial planning figures, not a statutory valuation, tax opinion or legal opinion.

1. Work delivered so far

Repository evidence as at 19 August 2026; active uncommitted work is included in readiness but not represented as a finished release.

Capability	Delivered evidence	State
Identity and onboarding	Credentials and OAuth foundations; verification, password reset, profile onboarding, session revocation and administrator MFA.	Strong beta
Member network	Profiles, follow/request/block controls, visibility settings, people discovery, warm introductions and interactive network graph.	Strong beta
Projects	Creation, drafts, roles, applications, invitations, teams, milestones, updates, completion, deletion lifecycle, funding interest and sharing.	Strong beta
Content and community	Posts, threaded replies, likes, reposts, mentions, saved items, notifications and public previews.	Strong beta
Matching and AI	Explainable scoring, people/project suggestions, vector embeddings, provider controls, blueprint generation and feedback records.	Beta
Messaging and meetings	Direct/group messaging, attachments, typing state, invitations, calendar integration, in-person maps, video/podcast rooms and chat.	Beta with scale limits
Administration and safety	Role hierarchy, audit log, moderation, sanctions, appeals, safety risks, official notices, analytics and algorithm controls.	Substantial; sign-off pending
SEO and discoverability	Global/page metadata, canonical URLs, index controls, Open Graph/Twitter cards and dynamic profile/share preview images.	Foundation present; technical SEO incomplete
Platform foundation	Next.js 16, React 19, Auth.js, Drizzle/PostgreSQL, Vercel deployment, Neon database, CI workflow and scheduled jobs.	Deployable

34,084 SOURCE / TEST / SQL LINES	34 DB MIGRATIONS	63 TEST FILES	8 days VISIBLE COMMIT WINDOW
--	----------------------------	-------------------------	--

Evidence quality

Production build: passes with 70 generated routes/pages and successful TypeScript compilation.

Automated tests: 229 of 230 pass. The failing assertion concerns the exact expression used for active-account verification.

Lint: 35 errors and 3 warnings, mainly inaccessible label/control associations plus four unused imports.

Working tree: 22 modified tracked files plus new draft/content files and a new migration. A release tag cannot be treated as immutable until this is reconciled and committed.

CI exists and is designed to run dependency audit, tests, lint, build and Playwright browser testing against PostgreSQL.

2. Cost of work completed

Equivalent commercial effort, not a claim of stopwatch hours. Rate: £75/hour, solo blended product, design and engineering rate.

Workstream	Hours	Value @ £75/h	% of total
Product discovery, requirements and architecture	95	£7,125	5%
Brand application, UX, responsive UI and accessibility	190	£14,250	11%
Frontend application and interaction design	370	£27,750	21%
Backend APIs, authentication and permissions	360	£27,000	20%
Database, search, analytics and recommendation systems	225	£16,875	13%
Messaging, meetings and external integrations	210	£15,750	12%
Administration, moderation, safety and security	185	£13,875	10%
Testing, deployment, migration tooling and documentation	155	£11,625	9%
Total equivalent work delivered	1,790	£134,250	100%

Why replacement effort is the right lens

The Git history shows an AI-accelerated delivery period, but elapsed calendar time is not an appropriate valuation method. A buyer receives the functioning codebase, schema, workflows, brand implementation, test suite and accumulated product decisions. The table estimates what a competent solo product engineer would need to recreate that asset to the observed scope and quality.


The £75/hour rate is deliberately blended. It remains lower than separately procuring product strategy, UX, senior full-stack engineering, security, QA and DevOps specialists. It also prevents the estimate from assuming agency overhead or a multi-person delivery team.

Sensitivity	Rate	Work-to-date value	10% of rounded current value
Conservative	£65/h	£116,350	about £12,200
Recommended	£75/h	£134,250	£14,000
Senior specialist	£90/h	£161,100	about £16,800

The final 10% figure changes if the parties choose a different rate or valuation basis. The recommended figure in this report uses £75/hour and the current rounded value of £140,000.

3. Readiness assessment

Two different questions matter: how much product exists, and how safely it can be operated for the public.

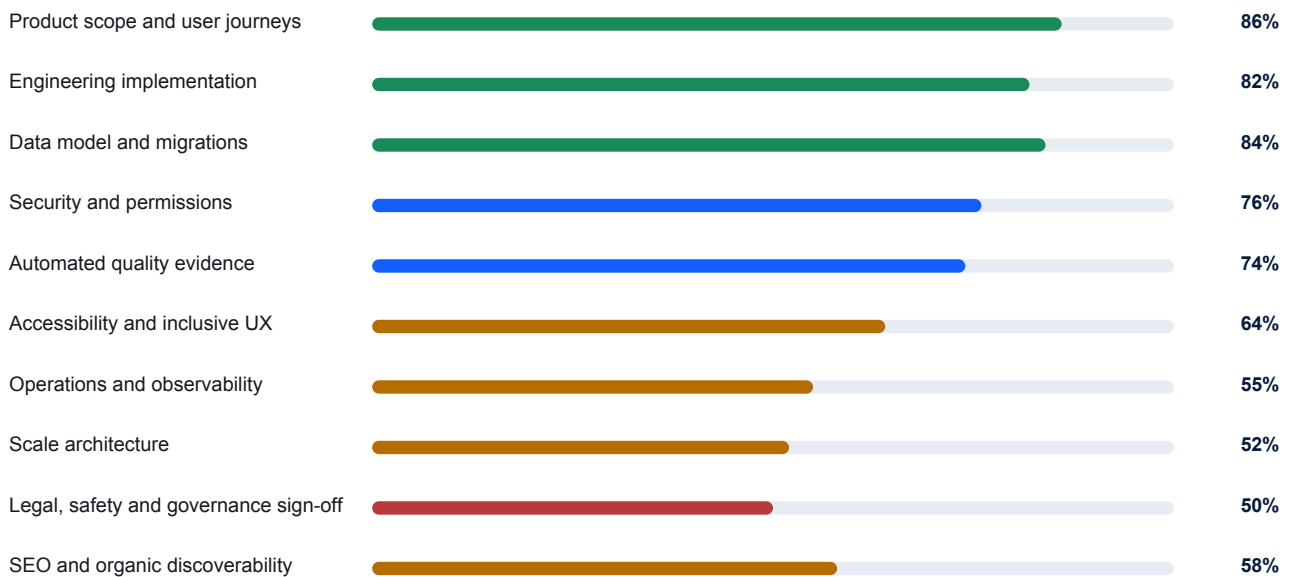

Readiness view	Score	Interpretation
Feature completion	84%	Most intended member, project, messaging, meeting, matching and admin journeys are represented.
Production readiness	63%	Buildable and deployable, but release gates, monitoring, storage, resilience and governance need completion.
Weighted overall	70%	Suitable for a controlled pilot with support; not yet a low-touch general public launch.

What 'completion' means in this report

Completion means a reproducible, supported public-launch release: all release gates pass, production configuration is verified, media and live features have an explicit scaling design, incident and recovery procedures exist, legal/safety owners have approved the service, and a measured pilot has demonstrated acceptable reliability.

It does not mean the product will never need further development. A live member network is an ongoing service with moderation, support, security, analytics and product iteration costs.

4. Gaps before completion

Priority work needed to convert the current late beta into an operationally complete launch.

Priority	Gap and required outcome	Effort	Acceptance evidence
P0	Stabilise release: reconcile uncommitted work; commit migration; fix 1 failing test, 35 lint errors and warnings; run full CI and browser suite.	70 h	Green CI on a tagged release; migration rehearsal succeeds.
P0	Production configuration: custom domain, verified email sender, OAuth applications, secret rotation, least-privilege access and spend alerts.	30 h	Production checklist signed; recovery contacts recorded.
P0	Operational resilience: error tracking, uptime checks, structured logs, alerts, backup policy, restore drill and incident runbook.	55 h	Alert test and timed restore exercise completed.
P0	Safety and data governance: accountable owner, processor register, DPIA/retention schedule, children's access/risk assessment and qualified UK review.	60 h	Approved records with review dates and escalation paths.
P1	Move profile/content media from base64 database fields to object storage/CDN with validation, lifecycle and deletion controls.	50 h	Load test confirms smaller DB responses and safe uploads.
P1	Live systems: replace database polling/mesh assumptions where required with managed real-time and SFU architecture, or explicitly cap rooms/pilot scope.	120 h	Concurrent room and message load tests meet SLOs.
P1	Accessibility, privacy and device QA: resolve labels, keyboard/screen-reader audit, mobile browsers and consent validation.	60 h	Documented WCAG-oriented audit; zero blocker defects.
P1	Performance and scale: representative seed data, query/index review, caching, queue/background job design and load tests.	35 h	P95 targets and capacity thresholds documented.
P1	Technical SEO: add sitemap and robots routes, structured data, canonical audit, indexation rules, Search Console/Bing setup, Core Web Vitals review and an organic reporting baseline.	30 h	Valid crawl/index controls, schema checks and search dashboards.
P2	Launch operations: analytics funnels, support workflow, moderation SLAs, user communications and launch dashboard.	20 h	Named owners, dashboards and weekly operating cadence.

Completion estimate

530 h BASE EFFORT	£39,750 BASE COST	£5,963 15% CONTINGENCY	£45,713 TOTAL BUDGET
-----------------------------	-----------------------------	----------------------------------	--------------------------------

Likely calendar: 8-12 weeks for one focused senior builder, depending on external legal review, OAuth approvals, live-media provider choice and the depth of pilot feedback. A narrow invite-only pilot can begin earlier after the P0 gates are satisfied.

5. Operating architecture and scale constraints

The current stack is economical at pilot size, but member growth changes the dominant costs.

Layer	Current implementation	Scale implication
Web and API	Next.js on Vercel with server-rendered and API routes.	Good elastic base. Costs follow requests, compute, memory and transfer.
Database	Neon PostgreSQL with Drizzle, pgvector, 70 tables and pooled connections.	Good early-stage base. Recommendation, graph and polling queries need measured indexing/caching.
Media	Profile images and some attachments are stored as base64/data URLs in PostgreSQL.	Base64 adds roughly one-third encoding overhead and makes DB rows/API responses expensive. Move to object storage before growth.
Messaging	API polling for messages/typing and database-backed notifications.	Polling multiplies requests and DB reads per active member. Managed realtime becomes economical as concurrency rises.
Video/podcast	Peer-to-peer WebRTC with database-backed signalling; online-room default capacity 8.	Mesh bandwidth grows rapidly with participants and does not provide TURN/SFU-grade reliability. Keep small or adopt a managed media layer.
AI	OpenAI or Gemini blueprint generation plus embeddings and scheduled recommendation jobs.	Embedding cost is low; repeated generation and re-index work need budgets, batching and per-member quotas.
Email	Resend transactional delivery for verification, password recovery and reminders.	Predictable until notification volume and marketing sends are added.
Operations	Vercel analytics and scheduled jobs; no dedicated error tracker found in the repository.	Add SLOs, alerting, trace/error correlation and spend alarms before public launch.

Primary cost equation

Monthly platform cost is driven by active usage, not registered-member count: daily active members x requests per session x data returned, plus database compute/storage, emails, AI calls, and live-media minutes. A dormant member costs almost nothing; a highly active video user can cost orders of magnitude more.

- Set budgets against MAU, DAU, messages, uploads, AI generations and live-media participant-minutes.
- At every stage, review actual Vercel and Neon usage before the next membership cohort is admitted.

6. Monthly operating and scaling costs

Planning ranges in GBP. Platform estimates include a production web plan, database, email, AI, monitoring, media/storage allowances and current architecture improvements where noted.

Stage	Usage assumption	Platform / month	Human operations / month	All-in / month	Platform / MAU
Controlled pilot	250 MAU; 50 DAU; small rooms; <3k emails	£35-£90	£520 (8 h)	£555-£610	£0.14-£0.36
Early growth	2,500 MAU; 500 DAU; 2m requests; 10k emails	£120-£350	£1,040 (16 h)	£1,160-£1,390	£0.05-£0.14
Growth	10,000 MAU; 2,000 DAU; 12m requests; 50k emails	£500-£1,800	£1,950 (30 h)	£2,450-£3,750	£0.05-£0.18
Scale	100,000 MAU; 20,000 DAU; 120m requests; 500k emails	£6,000-£20,000	£20k-£45k team	£26k-£65k	£0.06-£0.20

Expected cost mix

Cost centre	Pilot	10k MAU	100k MAU	Notes
Vercel web/API	£15-£40	£100-£450	£1,000-£5,000	Pro starts at \$20/month with usage credit; requests, compute and transfer grow with activity.
Neon PostgreSQL	£10-£25	£80-£350	£700-£3,000	Usage-based compute and storage; tune scale-to-zero, autoscaling and expensive queries.
Email	£0-£15	£15-£70	£70-£450	Resend free supports 3k emails; paid tiers start at \$20 for 50k.
AI recommendations	£2-£15	£40-£250	£400-£3,000	Embeddings are cheap; blueprint generation and repeated jobs dominate.
Media, realtime and CDN	£0-£10	£150-£600	£2,000-£9,000	Depends heavily on video minutes, TURN/SFU use, uploads and retention.
Monitoring, security and support tools	£8-£20	£80-£150	£1,000-£2,550	Error monitoring, uptime, log retention, moderation and support tooling.

Important: these are scenario ranges, not vendor quotes. They use a planning conversion of US\$1 = £0.76 and exclude VAT, payment processing, salaries outside the stated support allowance, marketing, insurance, legal advice and office costs.

Cost controls to implement

- Cap uploads, move binaries to object storage, compress images and apply retention rules.
- Use event-driven realtime instead of frequent polling; batch background recommendation jobs.
- Place per-member and per-project limits on AI generation, video duration and reminder volume.
- Set vendor spend alerts, database autoscaling ceilings and cohort-based launch gates.

7. Current value, completed value and buyout

A replacement-cost approach is the most defensible while there is no revenue, audited user traction or arm's-length investment price.

Valuation layer	Current	Completed	Basis
Direct equivalent build cost	£134,250	£174,000	1,790 delivered hours plus 530 completion hours, at £75/hour.
Delivery contingency	Included in rounding	£5,963	15% of remaining work to cover release and integration uncertainty.
Reusable IP / implementation uplift	Included in rounding	Included in rounding	Working system, brand implementation, schema, test suite, workflows and delivery acceleration.
Recommended project value	£140,000	£186,000	Rounded, commercially legible replacement value.
10% handover buyout	£14,000	£18,600	Exact 10% of the recommended project value.

Recommended buyout clause position

A current buyout price of £14,000 is recommended for a documented coding handover and transfer of the nice2 deployment projects and connected services to accounts controlled by the nice2 founders. The transaction is an operational handover, not merely delivery of a source-code archive.

If development fees are unpaid, add the work-to-date fee. This produces a present total of £148,250 excluding VAT. If the buyer has already paid the build fees, charging them again would double count; only the agreed handover buyout and any post-transfer support fee should remain.

Do not transfer personal vendor accounts or secrets informally. Use an asset schedule, founder-owned accounts, credential rotation, documented acceptance tests and a signed effective-transfer date.

Handover scope

Asset / service	Required handover action
Source and history	Transfer the Git repository, branches, release tag, documentation, schema, migrations, tests and agreed design/brand assets.
Vercel	Transfer the nice2 project to the founders' Vercel team; verify domains, environment variables, cron jobs, analytics, deployment permissions and billing ownership.
Database	Transfer or recreate the Neon project under founder control; verify pooled/unpooled connections, backups, restore access and migration state.
Email, identity and integrations	Transfer Resend sender/domain configuration and recreate Google/Microsoft OAuth applications with founder-owned credentials and redirect URLs.
AI and external services	Reissue OpenAI/Gemini and other provider keys under nice2 billing; set quotas, alerts and least-privilege access.
Domain, DNS and SEO	Transfer registrar/DNS control, verify canonical production URL, Search Console/Bing ownership, analytics access and sitemap submission.
Security and acceptance	Rotate every secret after transfer, remove IntAillium access when accepted, run smoke tests and sign an asset-and-access checklist.

CURRENT	AFTER COMPLETION
£14,000	£18,600
10% handover buyout	10% handover buyout

8. Completion plan and release gates

A practical sequence that protects value and prevents growth from magnifying known weaknesses.

Phase	Timing	Focus	Exit gate
1. Release stabilisation	Weeks 1-2	Freeze scope; reconcile tree; migrations; test/lint/E2E; production accounts; email/domain/OAuth.	Tagged release with all automated gates green.
2. Operational readiness	Weeks 2-4	Monitoring, alerts, backup/restore, security access, spend controls, incident/support runbooks.	Alert and restore drills passed; named owners on call.
3. Safety and governance	Weeks 2-5	DPIA, retention/processor register, children's assessment, moderation/appeal SLAs and qualified review.	Signed governance pack and launch decision.
4. Scale and SEO foundations	Weeks 4-8	Object storage, realtime strategy, queue/jobs, load tests, query tuning, sitemap/robots, schema and search tooling.	Capacity and technical SEO checks meet agreed thresholds.
5. Controlled pilot	Weeks 8-10	Invite cohort, support coverage, funnel/reliability measurement and incident learning.	Two stable weeks against SLOs; blocker defects closed.
6. Public launch	Weeks 10-12	Cohort expansion, communications, moderation capacity and cost review.	Formal go/no-go with budget and rollback plan.

Minimum launch KPIs

Availability and reliability: uptime target, error rate, P95 API latency and failed-job rate.

Safety and support: report response time, appeal handling, blocked abuse attempts and escalation time.

Product: onboarding completion, week-one activation, project application conversion and retained MAU.

Economics: platform cost per MAU, AI cost per generated blueprint, email per active member and live-media minutes.

Quality: zero release-blocking accessibility/security defects and no unresolved migration risk.

Advisory notice

Proceed with a controlled pilot after Phase 1-3 gates. Do not market the platform as fully complete or admit unrestricted public growth until object storage, live-system capacity and operational governance are evidenced.

9. Assumptions, exclusions and confidence

How to use these figures responsibly in a proposal, invoice or negotiation.

Area	Assumption / limitation
Time	No timesheet was present. Hours are equivalent replacement effort based on observed scope, not actual time worked.
Rate	£75/hour is the stated blended solo rate. Substitute a signed contractual rate only if the parties have already agreed one.
Valuation	Replacement cost is used because no audited revenue, churn, MAU, signed contracts or financing benchmark was supplied.
Usage	Operating ranges depend on MAU/DAU behaviour. Registered accounts alone are not a useful cost driver.
Vendor prices	Prices were checked on 19 August 2026 and can change. USD items use a planning conversion, not an accounting FX rate.
Legal	This report identifies governance work but is not legal advice. Qualified UK online-safety and data-protection review remains required.
Security	This was a repository and build audit, not a penetration test, threat-model workshop or production access-control audit.
Live service	No production billing exports, traffic analytics, database metrics or support data were supplied. Cost ranges should be replaced with actuals after the pilot.
Rights	Buyout effectiveness depends on signed chain-of-title, third-party licence compliance, asset schedule and precise transfer terms.

Confidence levels

High: repository scope, route/table/migration counts, build result, test/lint state and identified architecture patterns.

Medium: equivalent effort and remaining completion effort, because requirements and acceptance history were not supplied.

Medium-low: operating cost at 10k-100k MAU, because member behaviour, video use, content volume and service-level targets are unknown.

Commercial recommendation: £140,000 current value, £14,000 present handover buyout, and £186,000 completed value remain reasonable planning anchors under the stated assumptions.

10. Evidence and source notes

Primary technical evidence came from the local nice2 repository; vendor and regulatory figures use official sources.

Source	Used for
Local repository: README, package.json, database schema, migrations, routes, tests, CI, Vercel configuration and production build output	Scope, architecture, counts, feature evidence and current release readiness.
Vercel pricing and Fluid Compute pricing	Pro baseline, included usage model and compute/request cost drivers.
Neon pricing	Usage-based PostgreSQL compute, storage and representative load profiles.
Resend pricing	Transactional email free and paid tiers.
OpenAI GPT-4.1 mini and text-embedding-3-small	Configured AI model unit prices and the distinction between generation and embedding cost.
Ofcom protection of children duties	Need for access assessment, risk assessment, protective measures and records where children are likely to access the service.
ICO Age Appropriate Design Code	Age-appropriate privacy and design review context.

Prepared for discussion

This report is designed to support the coding and service-project handover to the nice2 founders, a commercial proposal or a buyout negotiation. Before signature, attach a detailed asset-and-access schedule and replace assumptions with payment history, production usage data and agreed acceptance criteria.

IntAillium

Product strategy, design and engineering assessment for nice 2 network
